
	Nombre	Duración	% Completado	Inicio	Fin	Predecesoras	Recursos	Jul L
1		☐ SIPOV FASE II	588.44d?	42%	03/08/2016	05/11/2018			
2	✓	☐ Fase de Preliminar	98.57d	100%	03/08/2016	19/12/2016			
3	✓	☐ Solicitud requerimiento Componente Tecnológico	98.57d	100%	03/08/2016	19/12/2016			
4	✓	☐ Revisión de requerimiento	98.57d	100%	03/08/2016	19/12/2016			
5	 ✓	Análisis de viabilidad	2d	100%	03/08/2016	04/08/2016		Comité Guia[1]	
6	✓	Reunión de entendimiento	1d	100%	16/12/2016	19/12/2016	5FI 95.57d	Líder de modern	
7	✓	Tramite Acta de Constitución de Proyecto	3d	100%	03/08/2016	05/08/2016		Líder de modern	
8	✓	☐ Fase de Inicio	1d	100%	03/08/2016	03/08/2016			
9	✓	Acta de Constitución Proyecto	1d	100%	03/08/2016	03/08/2016		Líder de modern	
10	✓	Kick Off Meeting	1d	100%	03/08/2016	03/08/2016		Líder de modern	
11	✓	Registro de interesados	1d	100%	03/08/2016	03/08/2016		Líder de modern	
12	✓	☐ Fase de Planeación	588.44d	100%	03/08/2016	05/11/2018			
13	✓	☐ Requerimientos funcionales	5d	100%	03/08/2016	09/08/2016			
14	✓	☐ Levantamiento de requerimientos	5d	100%	03/08/2016	09/08/2016			
15	✓	Reunion de levantamiento de requerimientos	1d	100%	03/08/2016	03/08/2016		Líder de modern	
16	✓	Documento de requerimientos funcionales	3d	100%	03/08/2016	05/08/2016		Líder equipo imp	
17	✓	Revisión, Ajustes y Aclaraciones	4d	100%	03/08/2016	08/08/2016		Líder de modern	
18	✓	Aprobación Documento de requerimientos funcion	5d	100%	03/08/2016	09/08/2016		Líder funcional[1	
19	✓	☐ Planeación de Proyecto	588.44d	100%	03/08/2016	05/11/2018			
20	✓	☐ Plan de Alcance	198.15d	100%	03/08/2016	08/05/2017			
21	✓	Definir Matriz de Requerimientos	2d	100%	03/08/2016	04/08/2016		Líder de modern	
22	✓	Definir SOW	1d	100%	16/12/2016	19/12/2016	21FI 95.57d	Líder de modern	
23	✓	Definición de la EDT	4d	100%	02/05/2017	08/05/2017	22FI 95.57d	Líder de modern	

24	✓	Plan de gestión de alcance del proyecto	4d	100%	03/08/2016	08/08/2016		Líder de modern
25	✓	☐ Plan de Tiempo	101.57d	100%	18/09/2017	07/02/2018		
26	✓	Definición del Cronograma	3d	100%	18/09/2017	21/09/2017	23FI 95.57d	Líder de modern
27	✓	Plan de gestión del cronograma	3d	100%	02/02/2018	07/02/2018	26FI 95.57d	Líder de modern
28	✓	☐ Planes subsidiarios	97.57d	100%	20/06/2018	05/11/2018	27FI 95.57d	
29	✓	Plan de gestión al riesgo	1d	100%	20/06/2018	21/06/2018		Líder de modern
30	🇨🇺 ✓	Plan de Gobierno	1d	100%	02/11/2018	05/11/2018	29FI 95.57d	Líder de modern
31	✓	Plan de Comunicaciones	1d	100%	20/06/2018	21/06/2018		Líder de modern
32	✓	Plan de gestión de la calidad	2d	100%	20/06/2018	22/06/2018		Líder de modern
33	✓	Plan de gestión del Proyecto	1d	100%	20/06/2018	21/06/2018		Líder de modern
34		☐ Fase de Ejecución	114d?	34%	03/08/2016	09/01/2017		
35		☐ Re-estructuración de proyecto	43d	84%	03/08/2016	30/09/2016		
36	✓	Modelo de Base de Datos	3d	100%	03/08/2016	05/08/2016		Líder equipo imp
37	✓	Generación de Vistas y Controladores	43d	100%	03/08/2016	30/09/2016		Líder equipo imp
38		Documentación de Casos de Uso	2d	0%	03/08/2016	04/08/2016		Líder equipo imp
39		Diseño de Programas de Importación	7d	0%	03/08/2016	11/08/2016		Líder equipo imp
40	✓	SIPOV completamente rediseñado	1d	100%	03/08/2016	03/08/2016		Líder equipo imp
41		☐ Desarrollo Requerimientos Fase II SIPOV	101d?	26%	03/08/2016	21/12/2016		
42	✓	☒ Motor de Búsqueda	3d	100%	03/08/2016	05/08/2016		
44	✓	☒ Notificaciones OAJ	3d	100%	03/08/2016	05/08/2016		
46	✓	☒ Reportes Actividades Mensuales	10d	100%	04/11/2016	17/11/2016		
48	✓	☒ Ajustes y Configuración de SIPOV	2d	100%	08/09/2016	09/09/2016		
50	✓	☒ Checkpoint 1	1d	100%	03/08/2016	03/08/2016		
52	✓	☒ Organización de Formularios SIPOV	67d	100%	03/08/2016	03/11/2016		
55	✓	☒ Adición de Documentos a un Fallo	2d	100%	31/10/2016	01/11/2016		

57	✓	⊕ Adición de Beneficiarios	4d	100%	18/11/2016	23/11/2016		
59		⊕ Adición de estados al fallo	74d?	0%	24/08/2016	05/12/2016		
61		⊕ Pruebas funcionales Usuario Funcional	12d	0%	06/12/2016	21/12/2016		
65		⊖ Fase de Transición	29d	0%	30/11/2016	09/01/2017		
66		⊖ Sincronización SIPOV I con SIPOV II	29d	0%	30/11/2016	09/01/2017		
67		⊖ Migración de Datos	23d	0%	30/11/2016	30/12/2016		
68		Congelamiento temporal de plataforma	23d	0%	30/11/2016	30/12/2016		Líder equipo imp
69		Extracción de Datos SIPOV I	4d	0%	02/12/2016	07/12/2016		Líder equipo imp
70		Importación SIPOV I a SIPOV II	6d	0%	09/12/2016	16/12/2016		Líder equipo imp
71		Verificación Importación con usuario funcional	2d	0%	20/12/2016	21/12/2016		Líder equipo imp
72		⊖ Salida a producción	20d	0%	13/12/2016	09/01/2017		
73		Documentación Infraestructura	9d	0%	13/12/2016	23/12/2016		Líder equipo imp
74		Aprobación RFC para paso a producción	5d	0%	26/12/2016	30/12/2016		Líder equipo imp
75		Despliegue sobre servidores Productivos	3d	0%	04/01/2017	06/01/2017		Líder equipo imp
76		SIPOV FASE II En producción	1d	0%	09/01/2017	09/01/2017		Líder equipo imp
77		⊖ Fase de Cierre	31d	0%	10/01/2017	21/02/2017		
78		⊖ Divulgación SIPOV II	16d	0%	10/01/2017	31/01/2017		
79		⊖ Divulgación SIPOV II a MADR	16d	0%	10/01/2017	31/01/2017		
80		Presentación de Proyecto SIPOV II a MADR	4d	0%	10/01/2017	13/01/2017		Líder de modern
81		Divulgación SIPOV II a entidades Adscritas y Vincu	12d	0%	16/01/2017	31/01/2017		Líder de modern
82		⊖ Cierre de Proyecto	15d	0%	01/02/2017	21/02/2017		
83		Aceptación funcional	1d	0%	01/02/2017	01/02/2017		Líder de modern
84		Informe de Cierre de Proyecto	3d	0%	02/02/2017	06/02/2017		Líder de modern
85		Lecciones aprendidas	3d	0%	02/02/2017	06/02/2017		Líder de modern
86		Cierre de proyecto	11d	0%	07/02/2017	21/02/2017		Líder de modern

[illegible]

◆ 08/08/2016 Líder de modernización[1]

◆ 05/08/2016 Líder equipo implemetador[1]

◆ 04/08/2016 Líder equipo implemetador[1]



◆ 11/08/2016 Líder equipo implemetador[1]

◆ 03/08/2016 Líder equipo implemetador[1]


05/08/2016

05/08/2016


03/08/2016

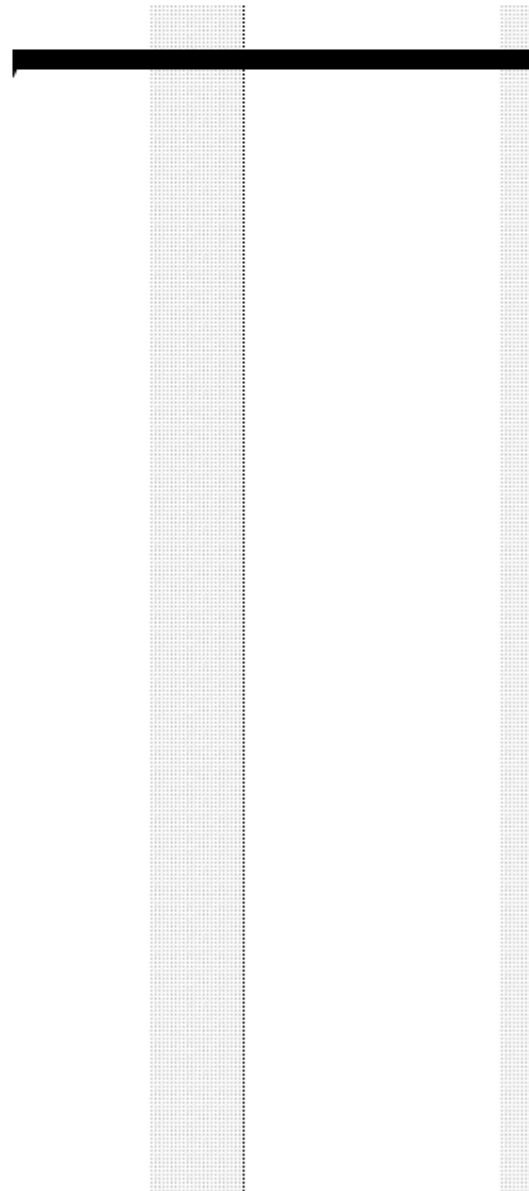

[illegible]

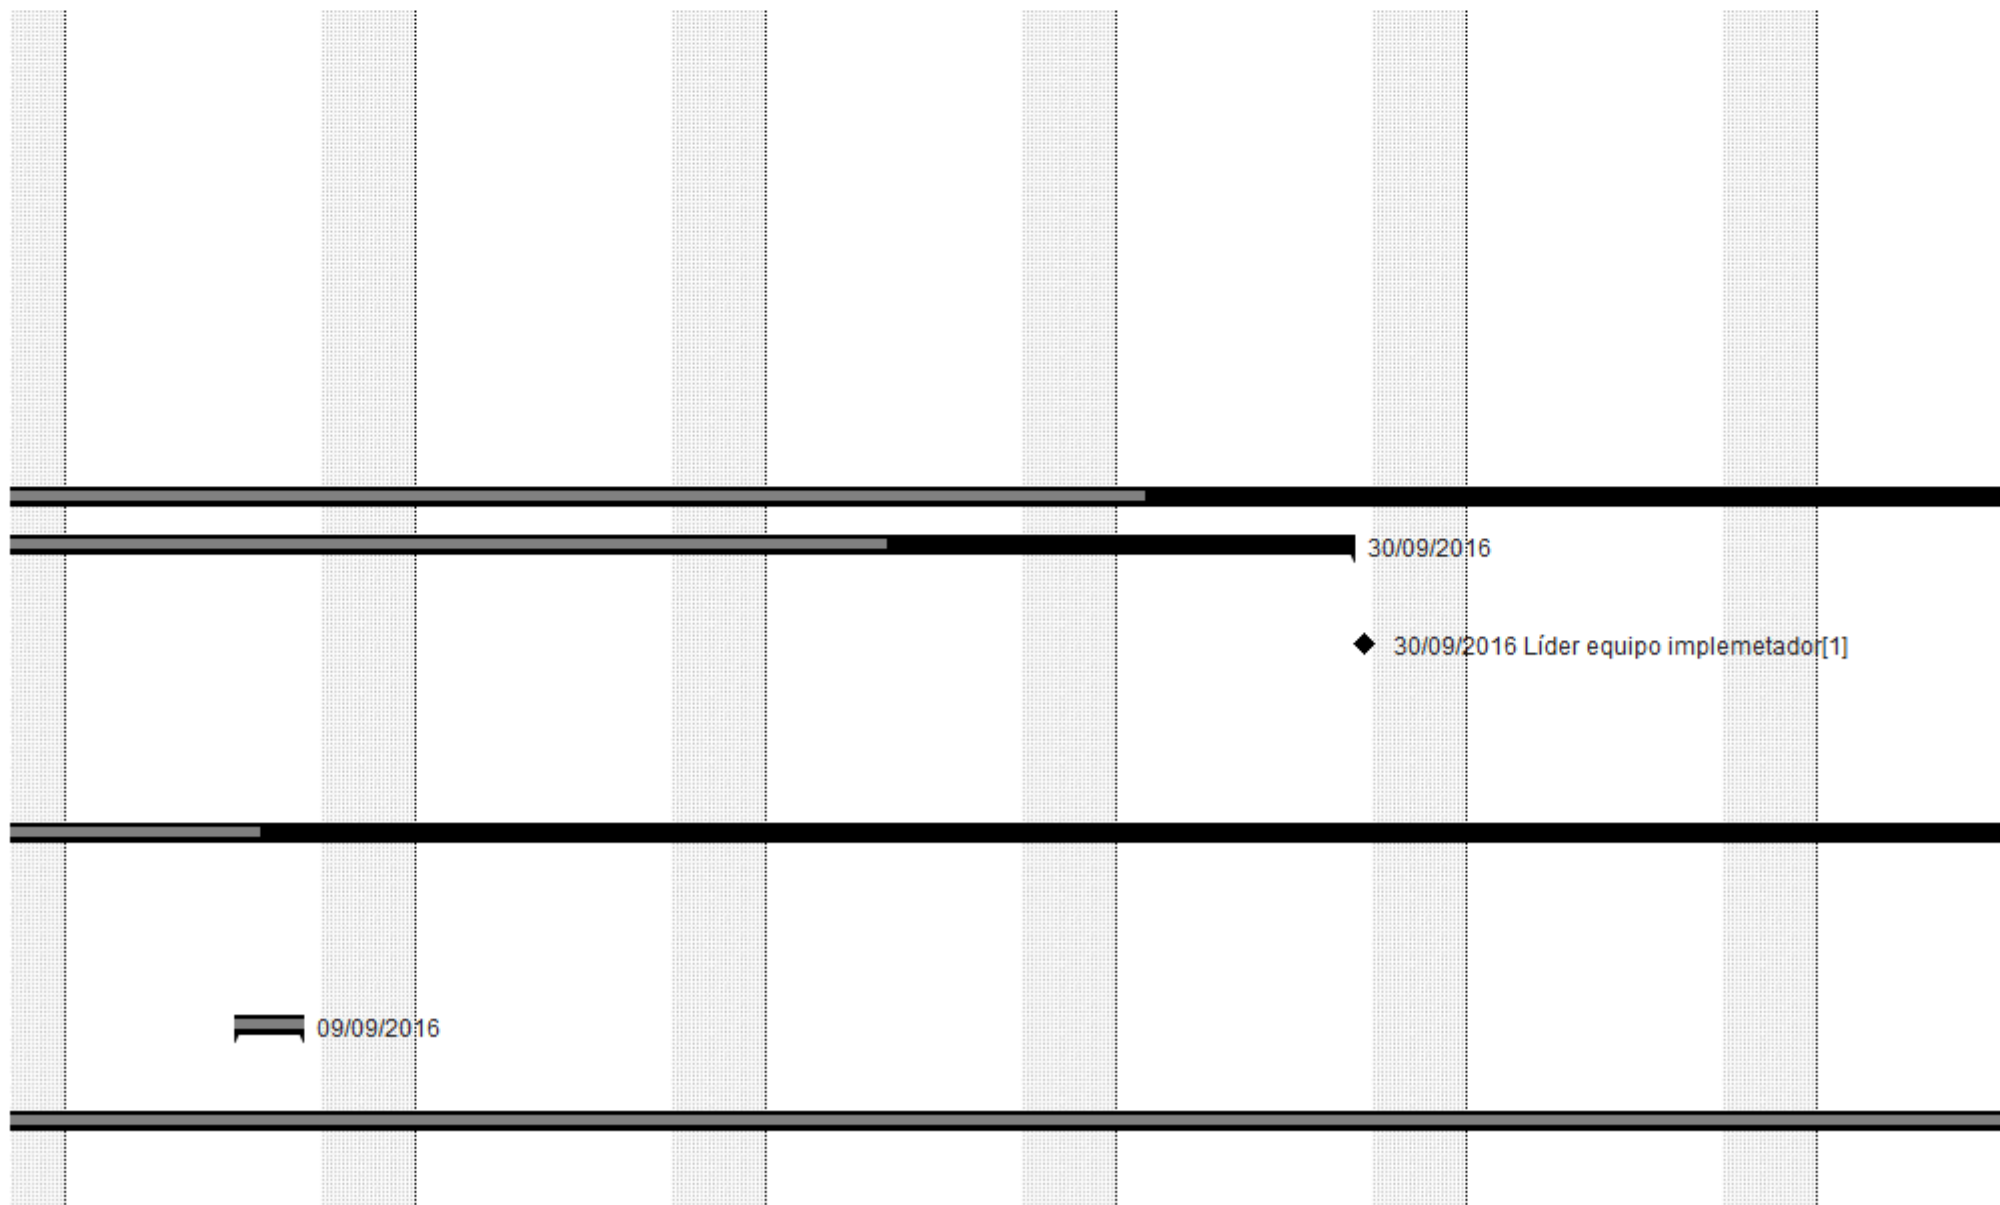


[illegible]

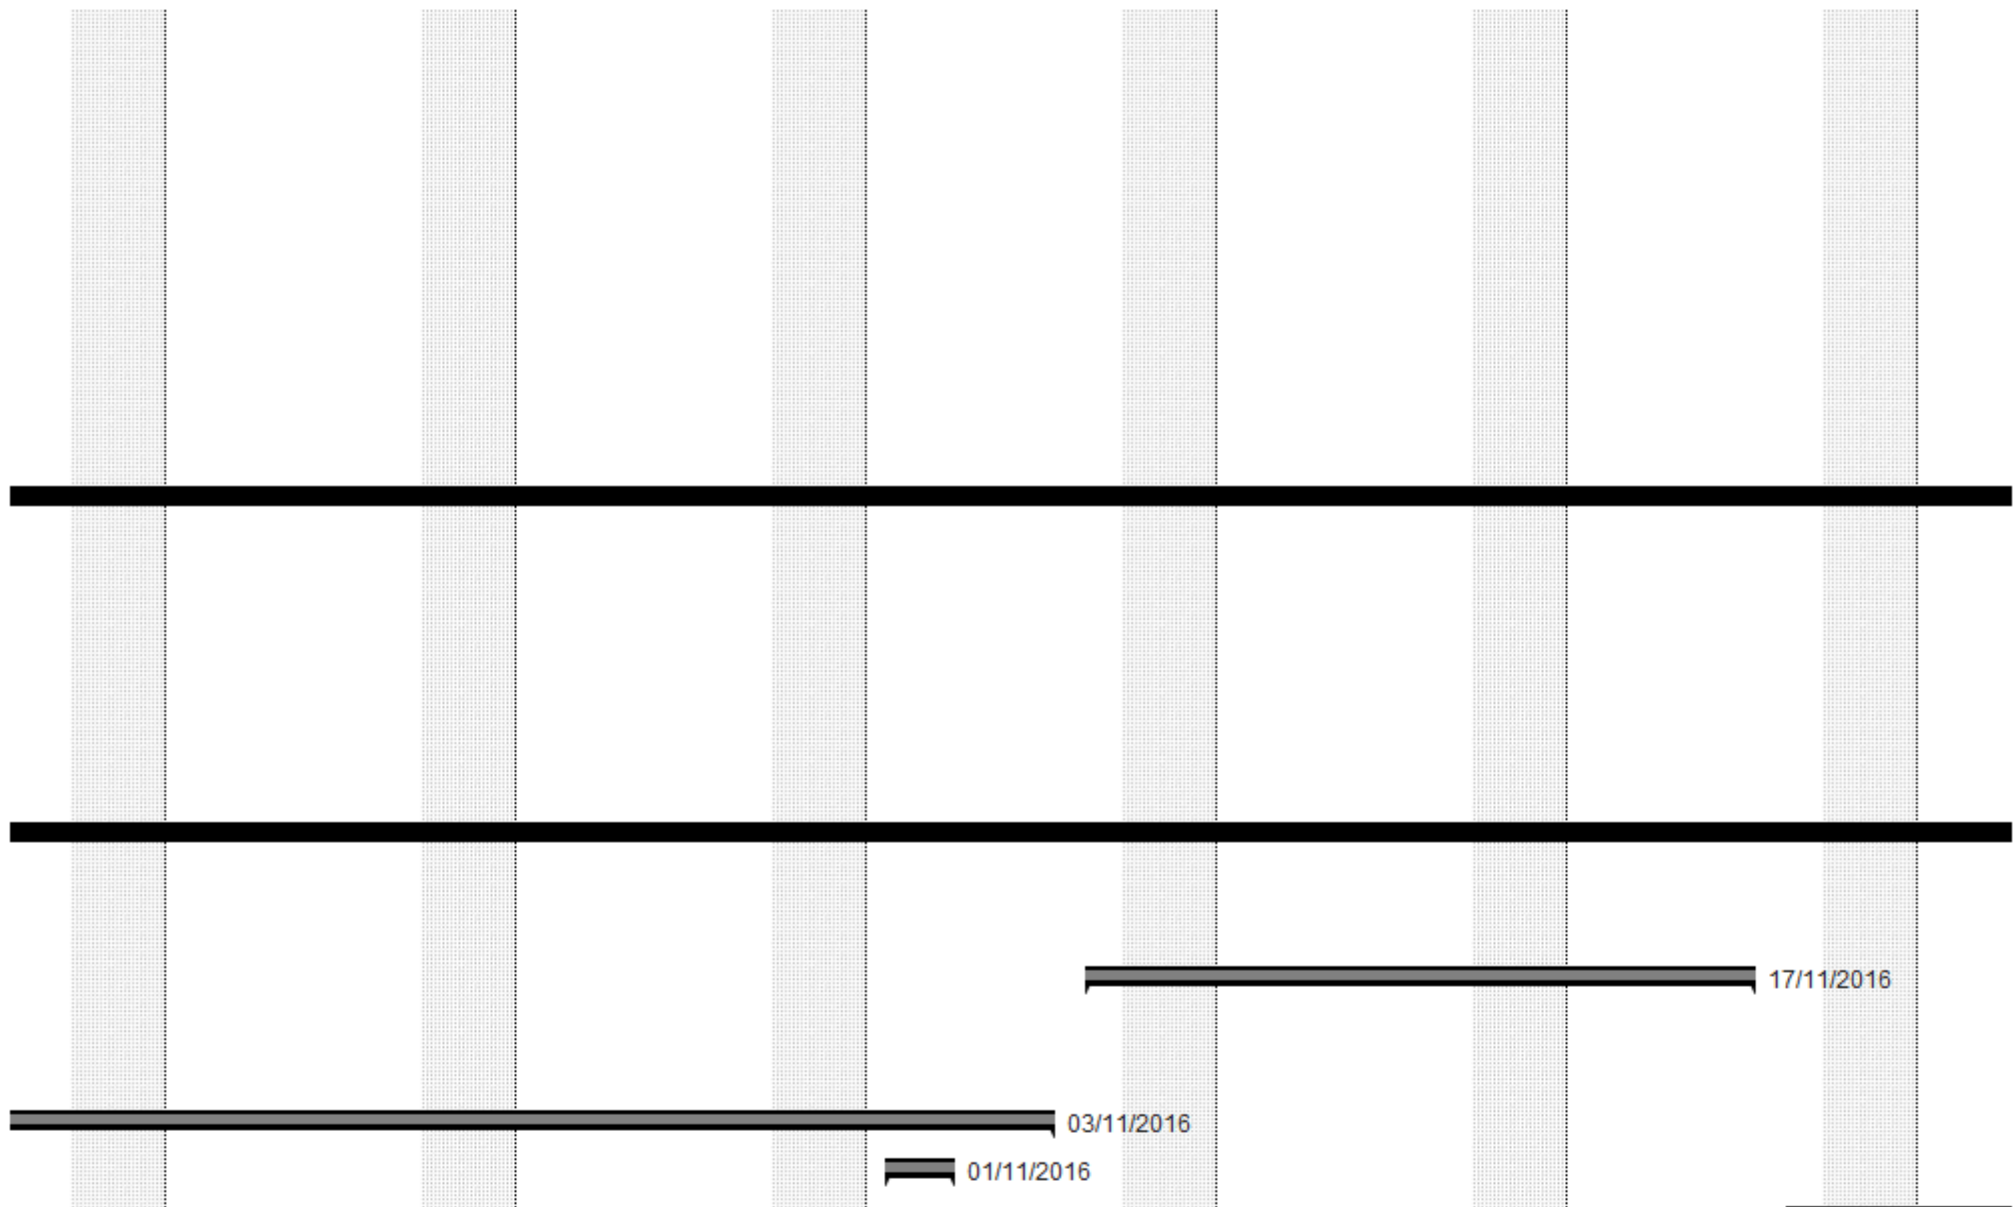


- Nov 27 '16					Nov 28 - Dic 4 '16					Dic 5 - Dic 11 '16					Dic 12 - Dic 18 '16					Dic 19 - Dic 25 '16					Dic 26 - Ene 1 '17							
X	J	V	S	D	L	M	X	J	V	S	D	L	M	X	J	V	S	D	L	M	X	J	V	S	D	L	M	X	J	V	S	D



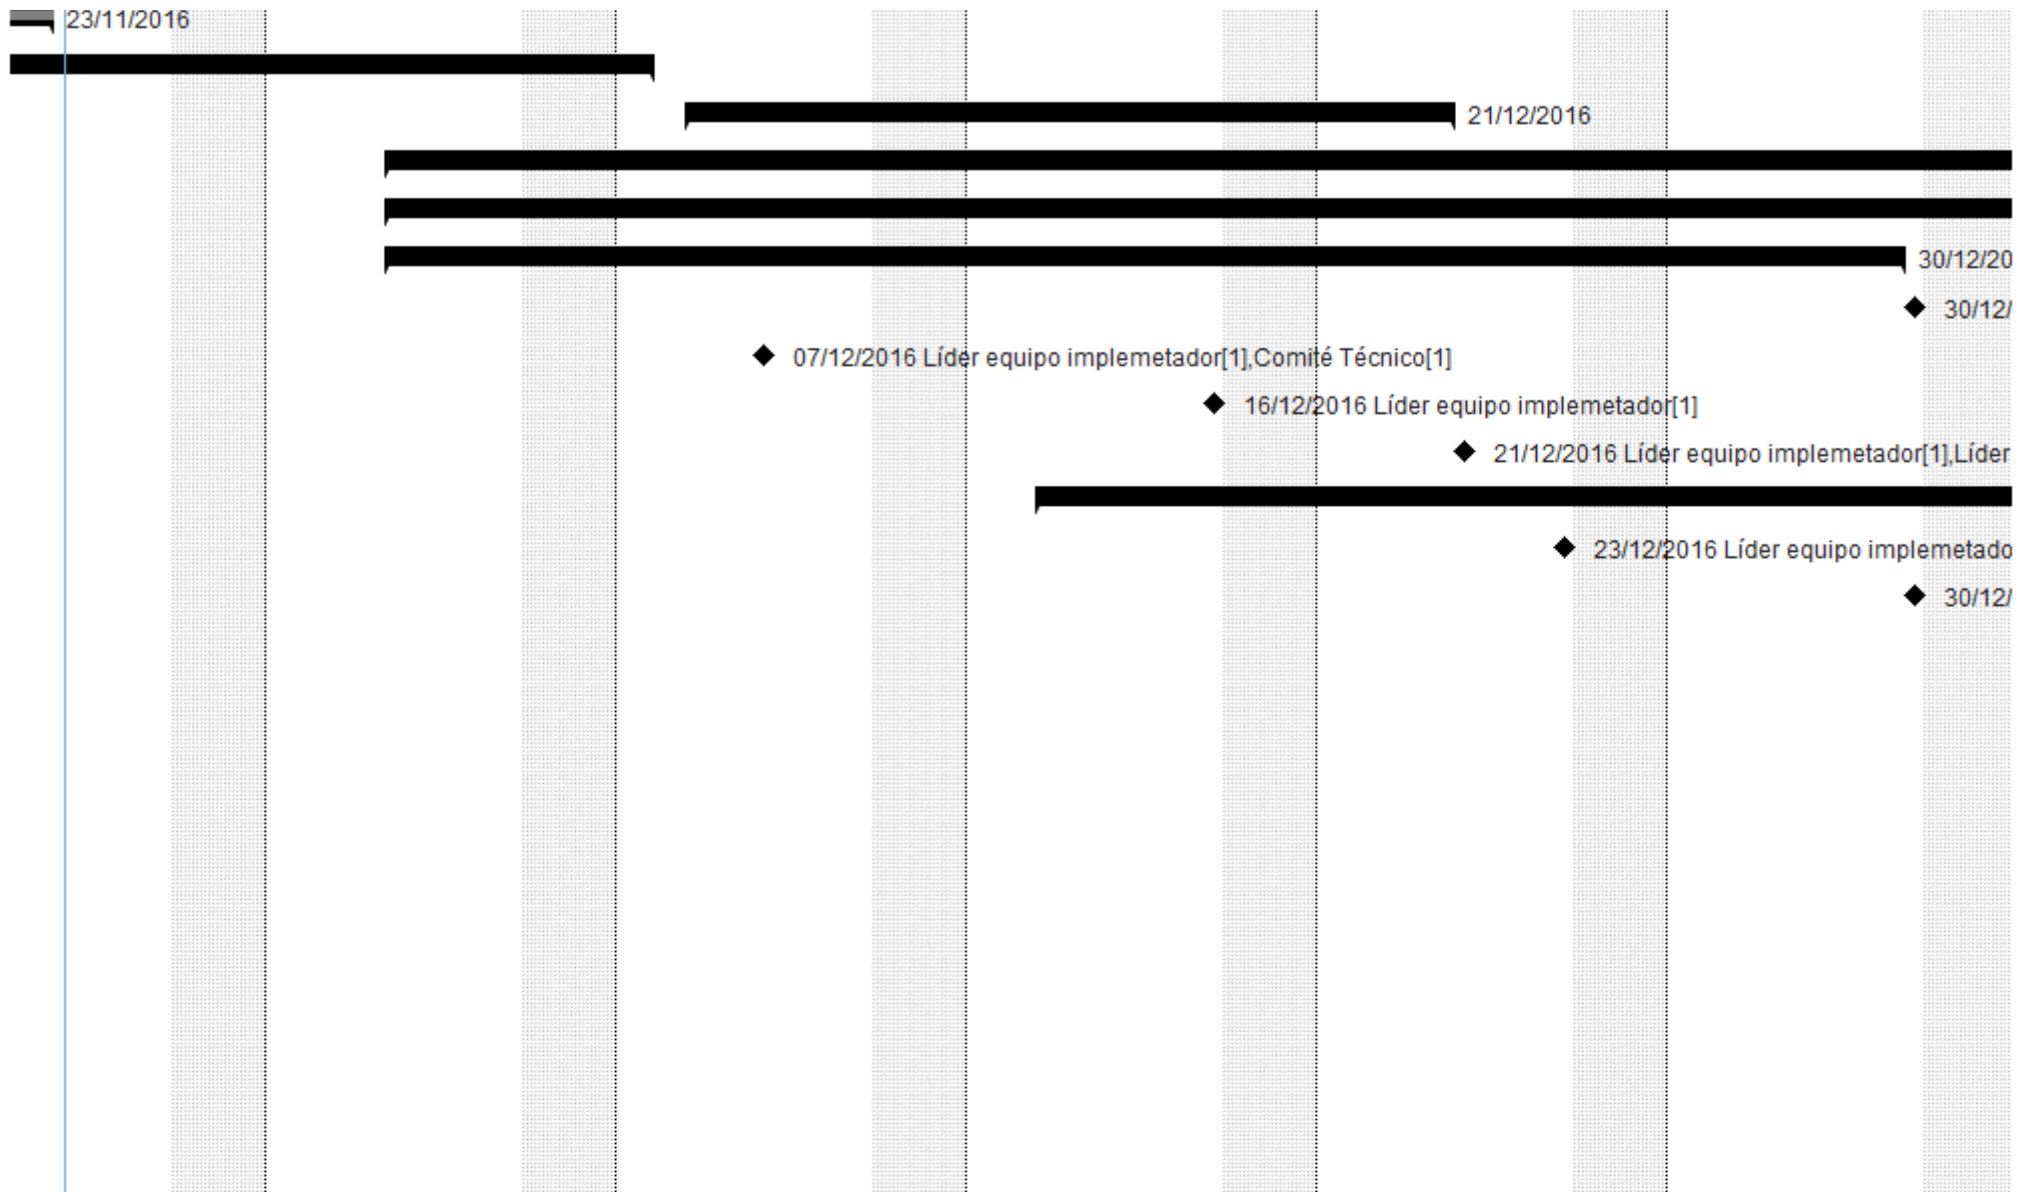

[illegible]

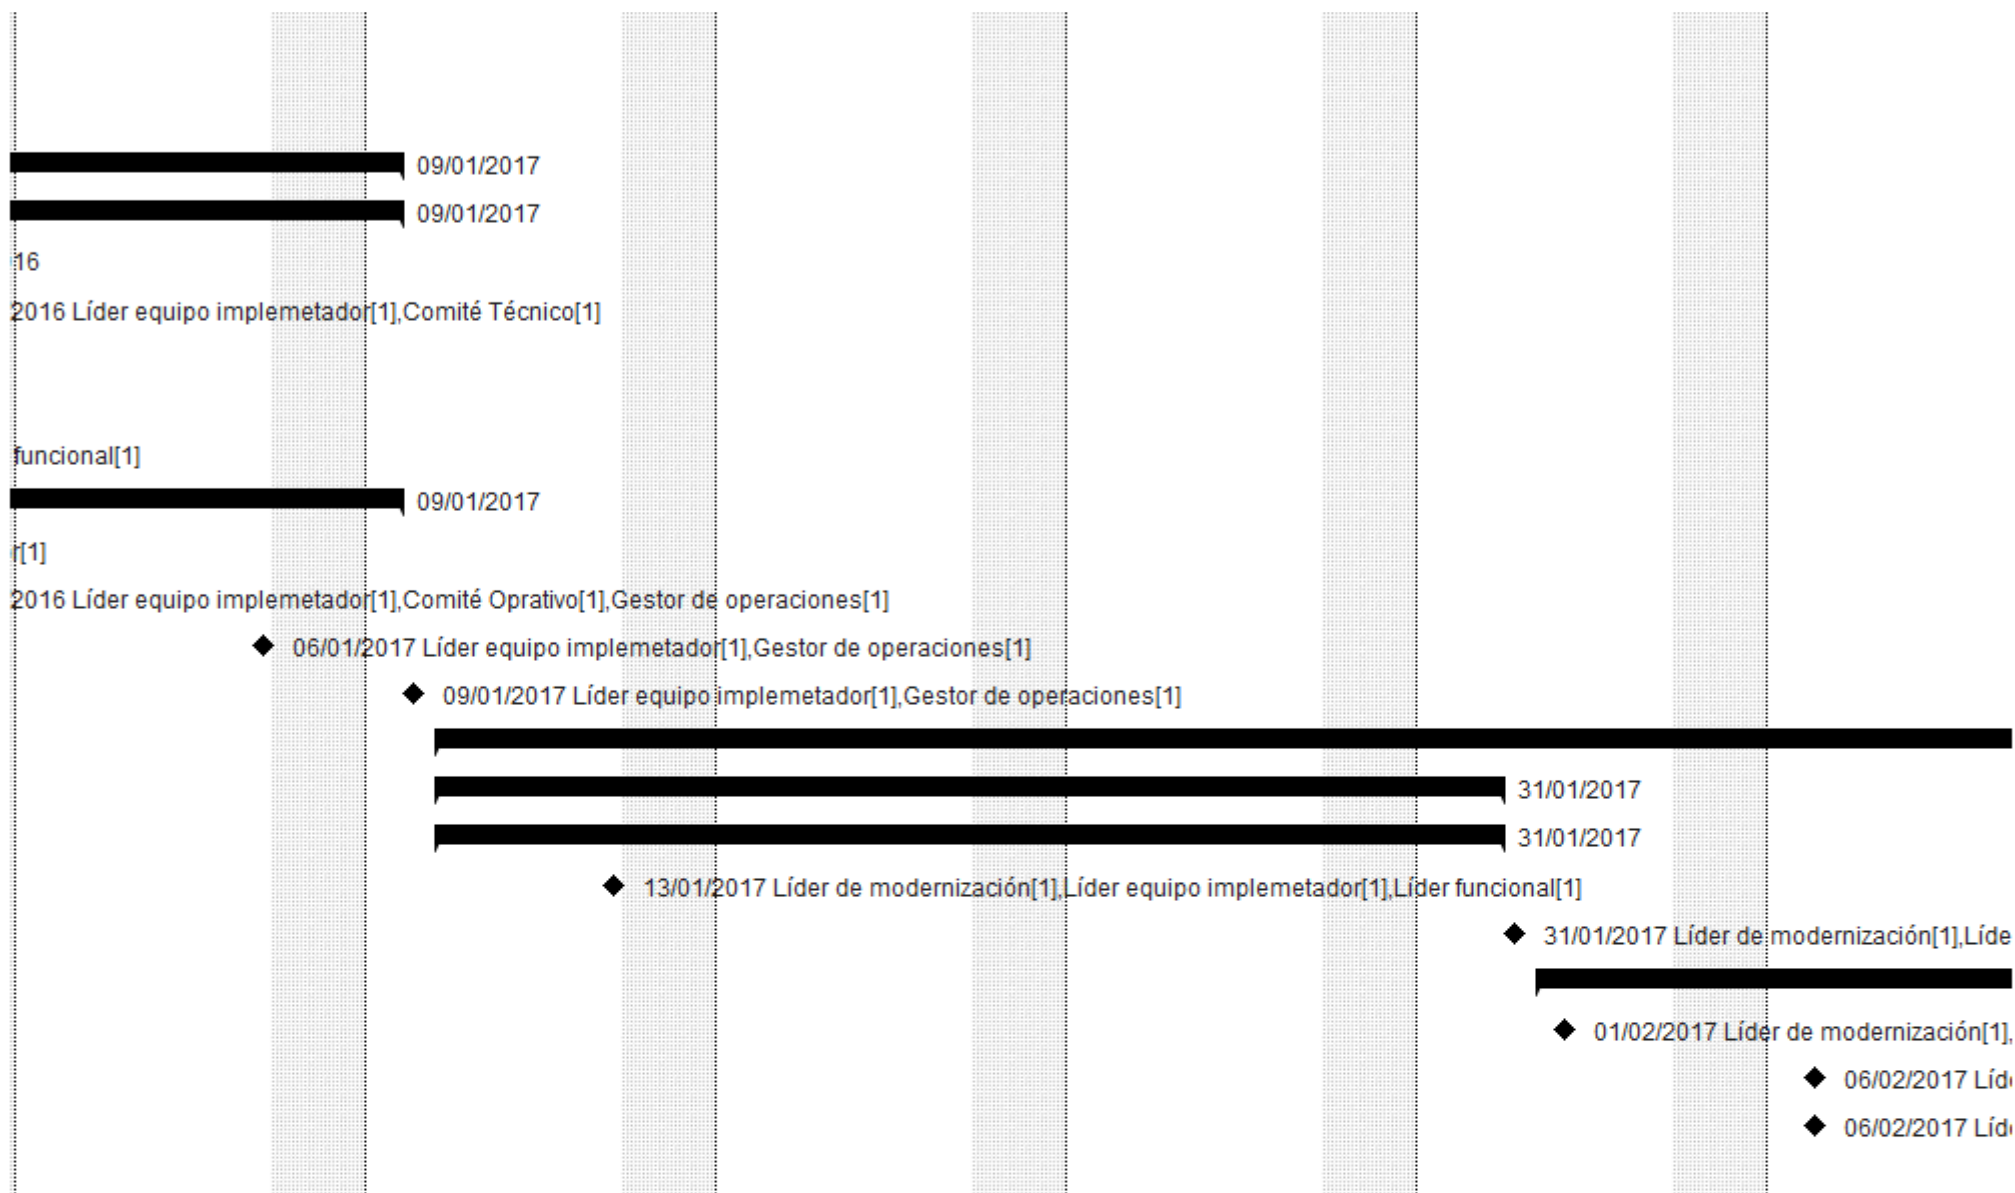

[illegible]



















[illegible]







--	--	--	--	--	--	--

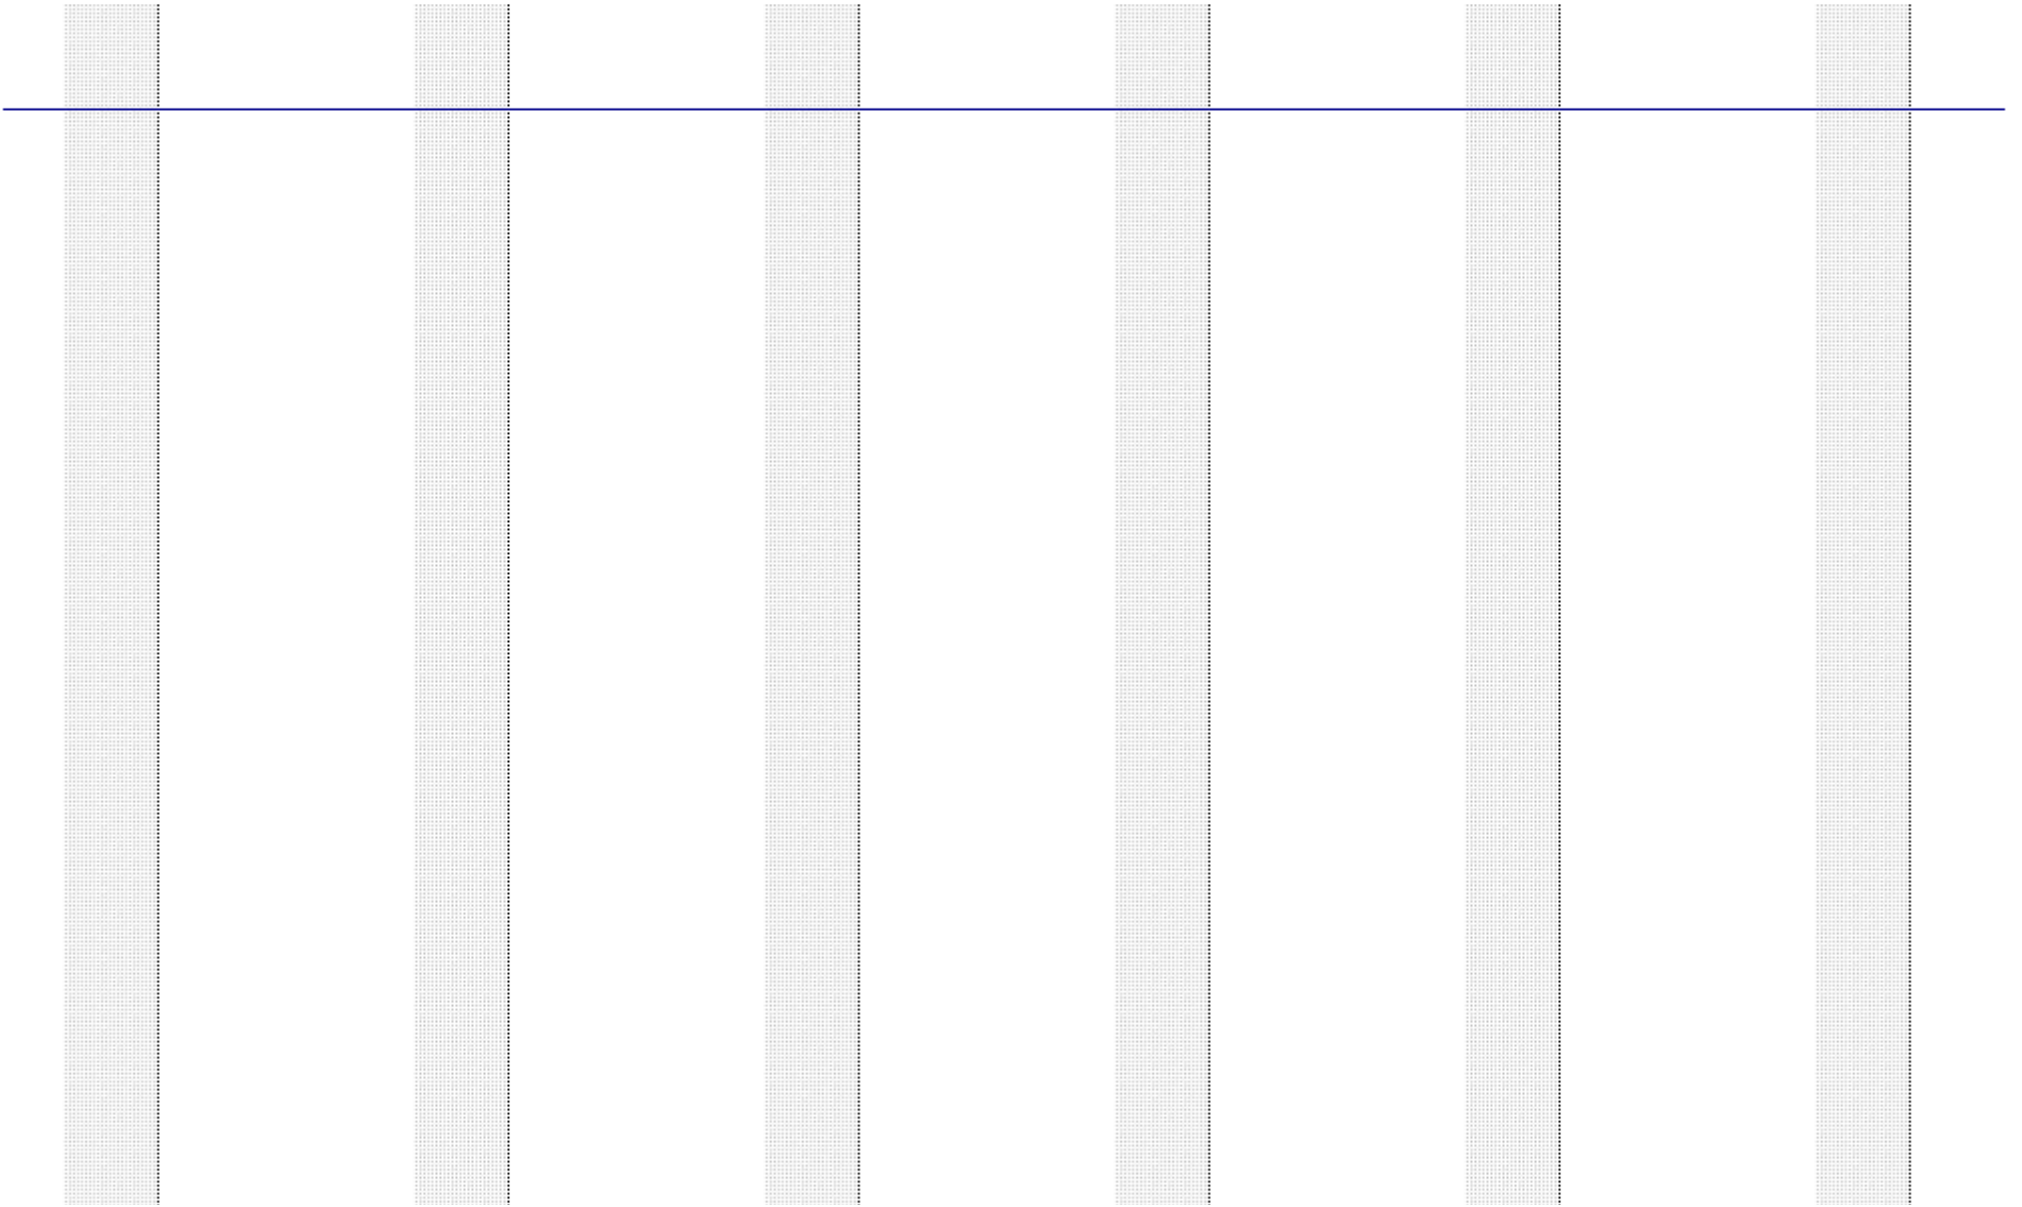






[illegible]

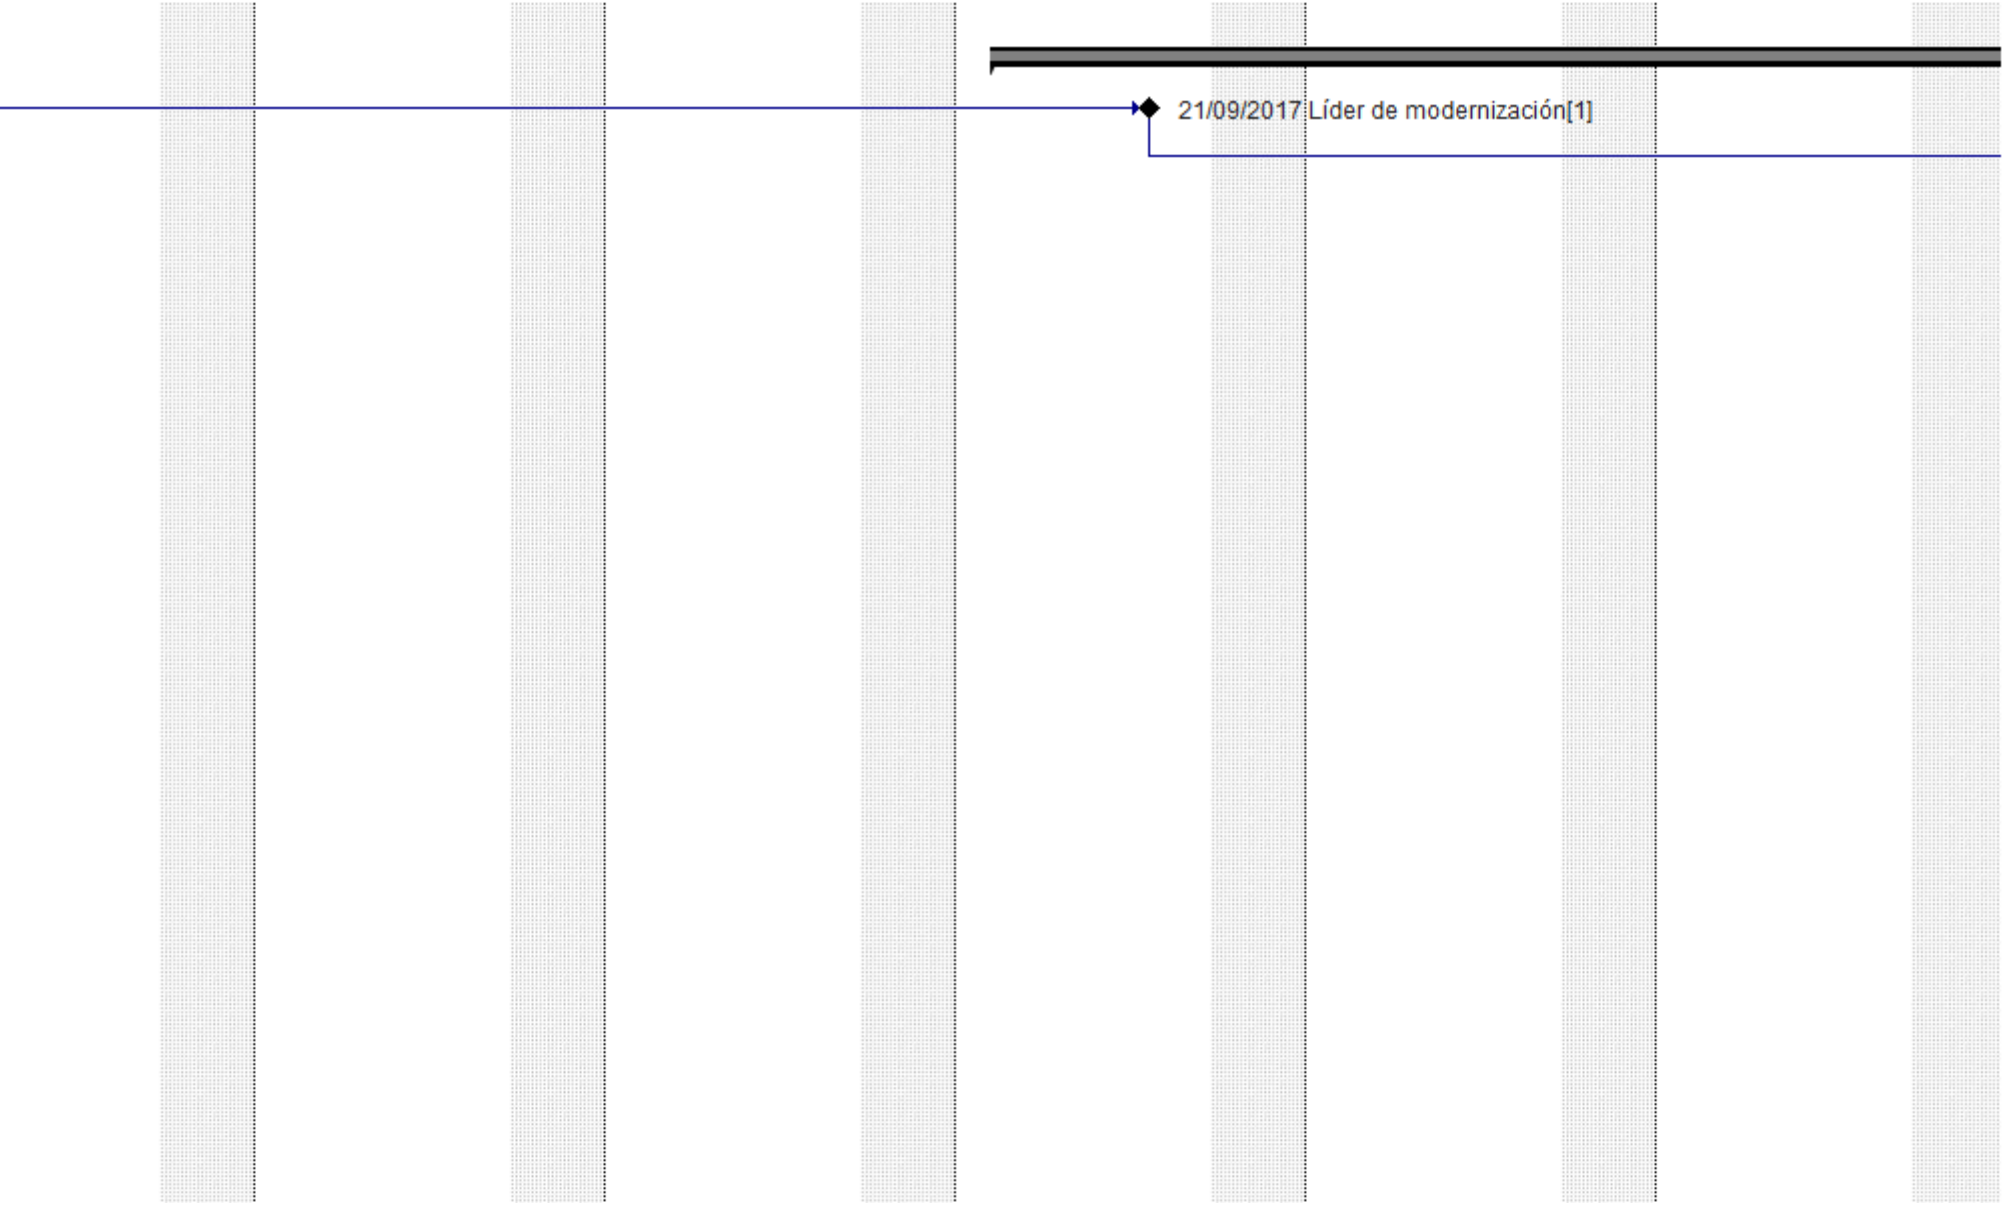



[illegible]

[illegible]






[illegible]




[illegible]










[illegible]



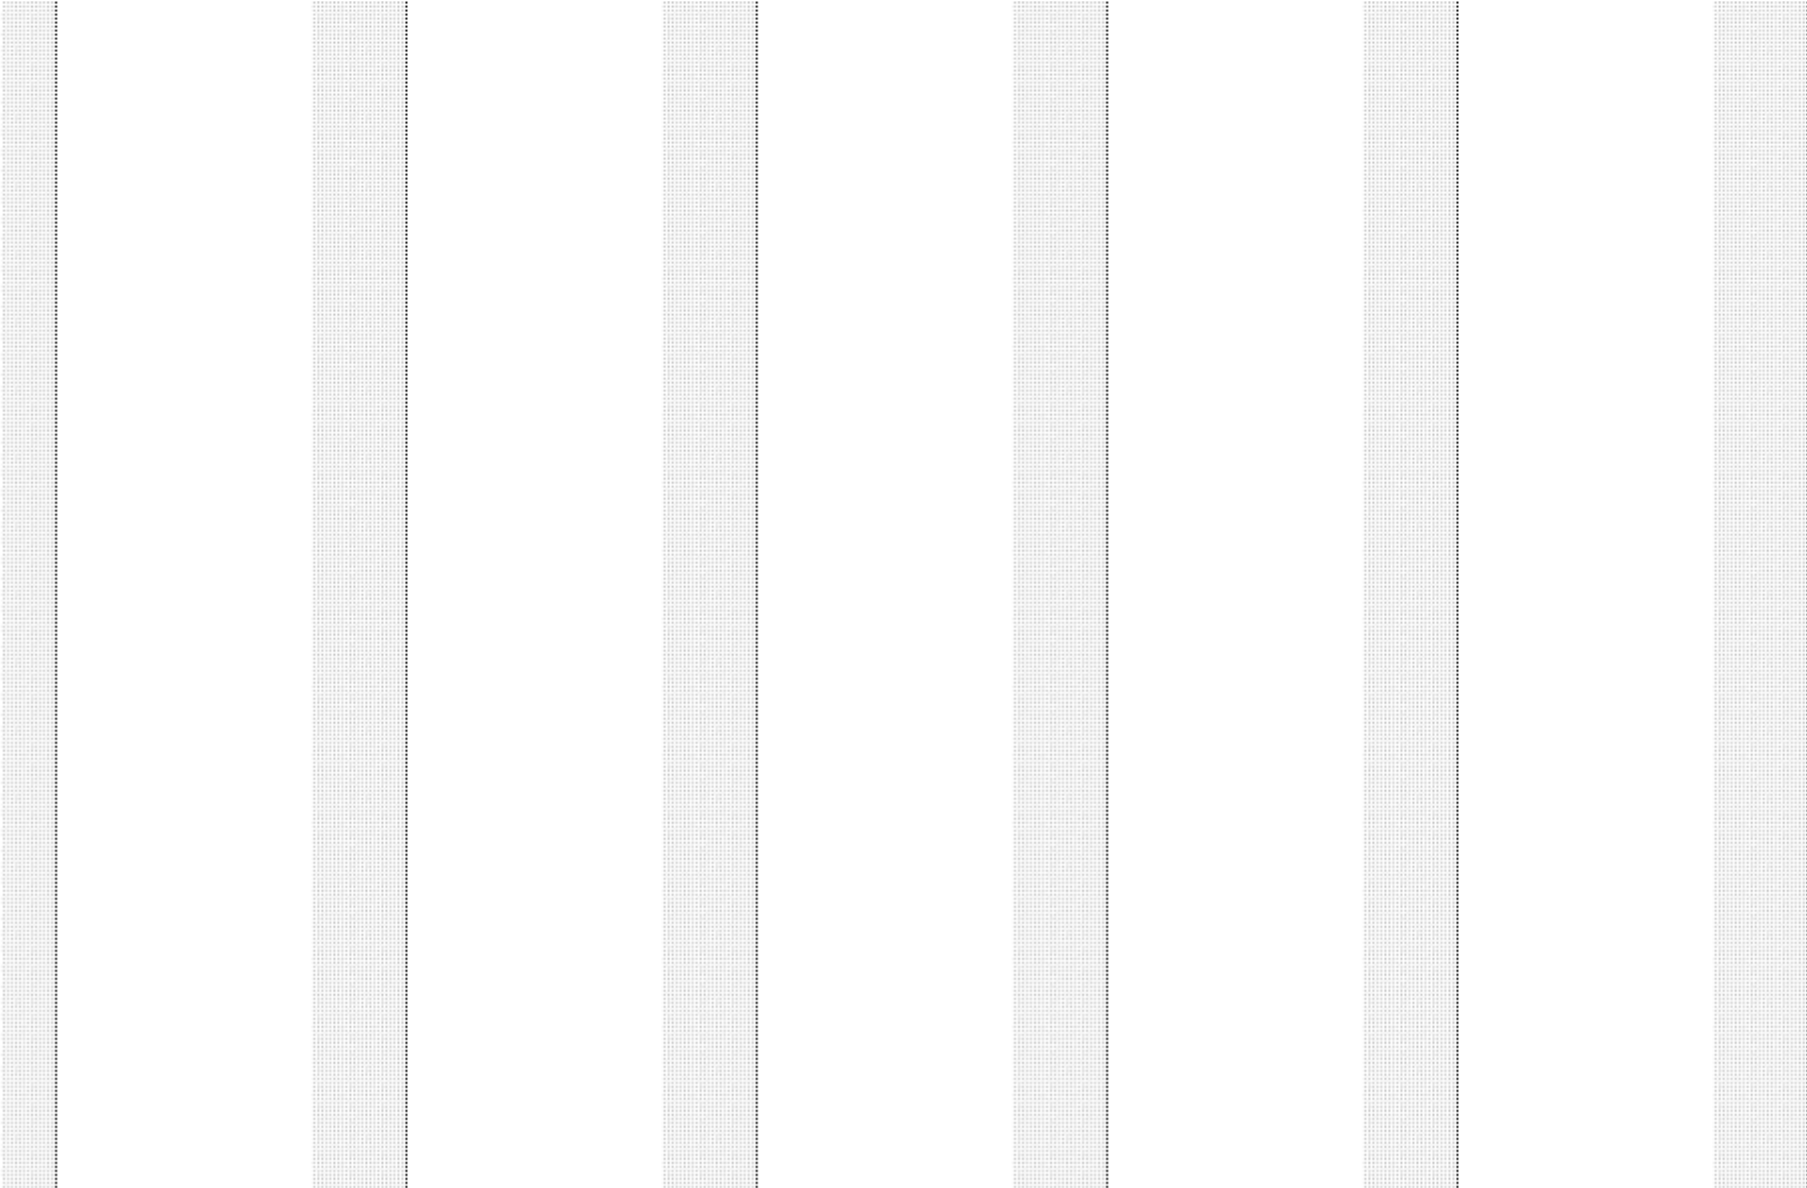


[illegible]

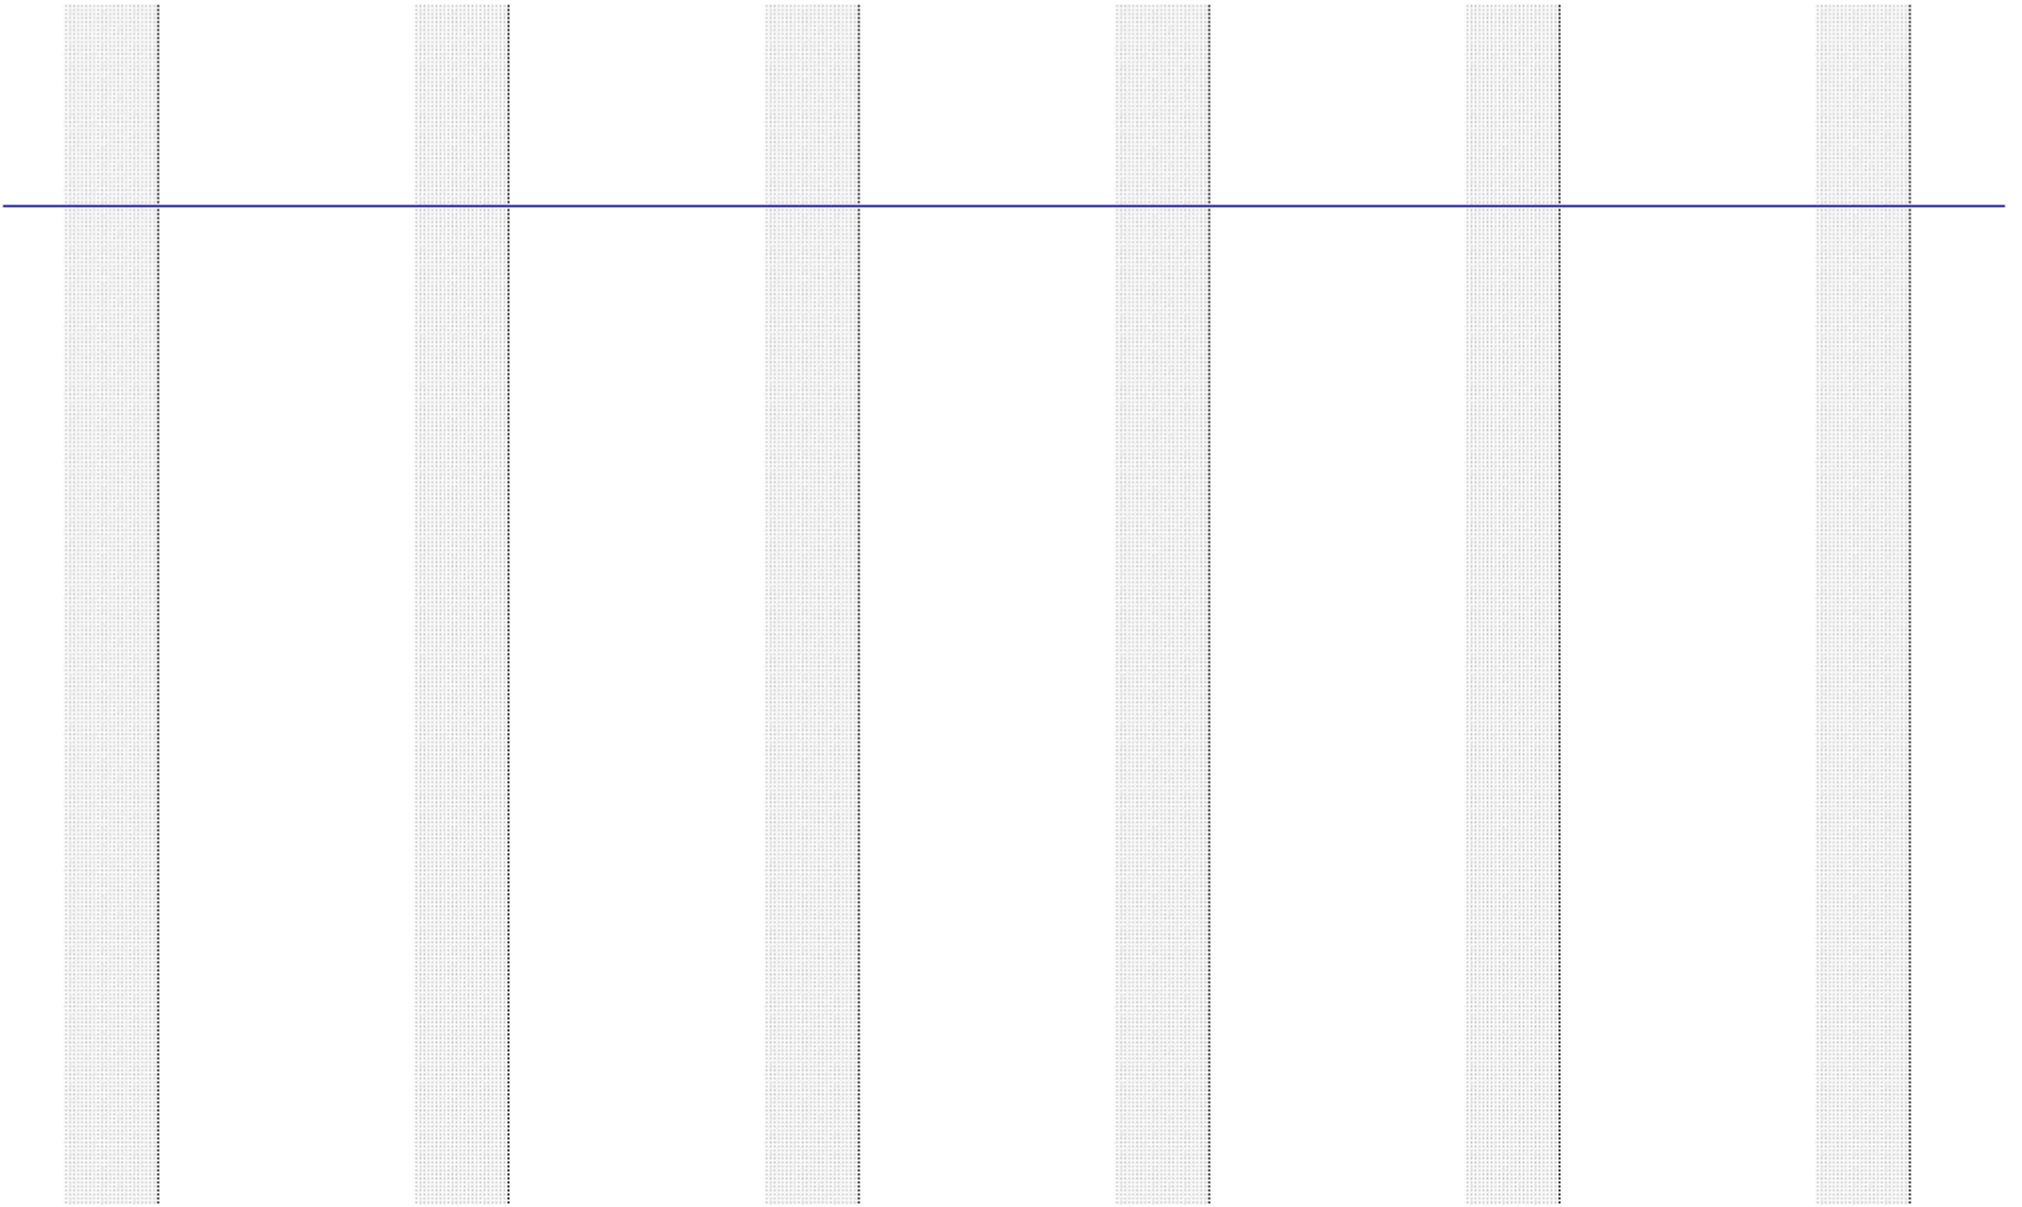



Jun 10 '18					Jun 11 - Jun 17 '18					Jun 18 - Jun 24 '18					Jun 25 - Jul 1 '18					Jul 2 - Jul 8 '18					Jul 9 - Jul 15 '18							
X	J	V	S	D	L	M	X	J	V	S	D	L	M	X	J	V	S	D	L	M	X	J	V	S	D	L	M	X	J	V	S	D




◆ 21/06/2018 Líder de modernización[1]


◆ 21/06/2018 Líder de modernización[1]

◆ 22/06/2018 Líder de modernización[1]

◆ 21/06/2018 Líder de modernización[1]



[illegible]

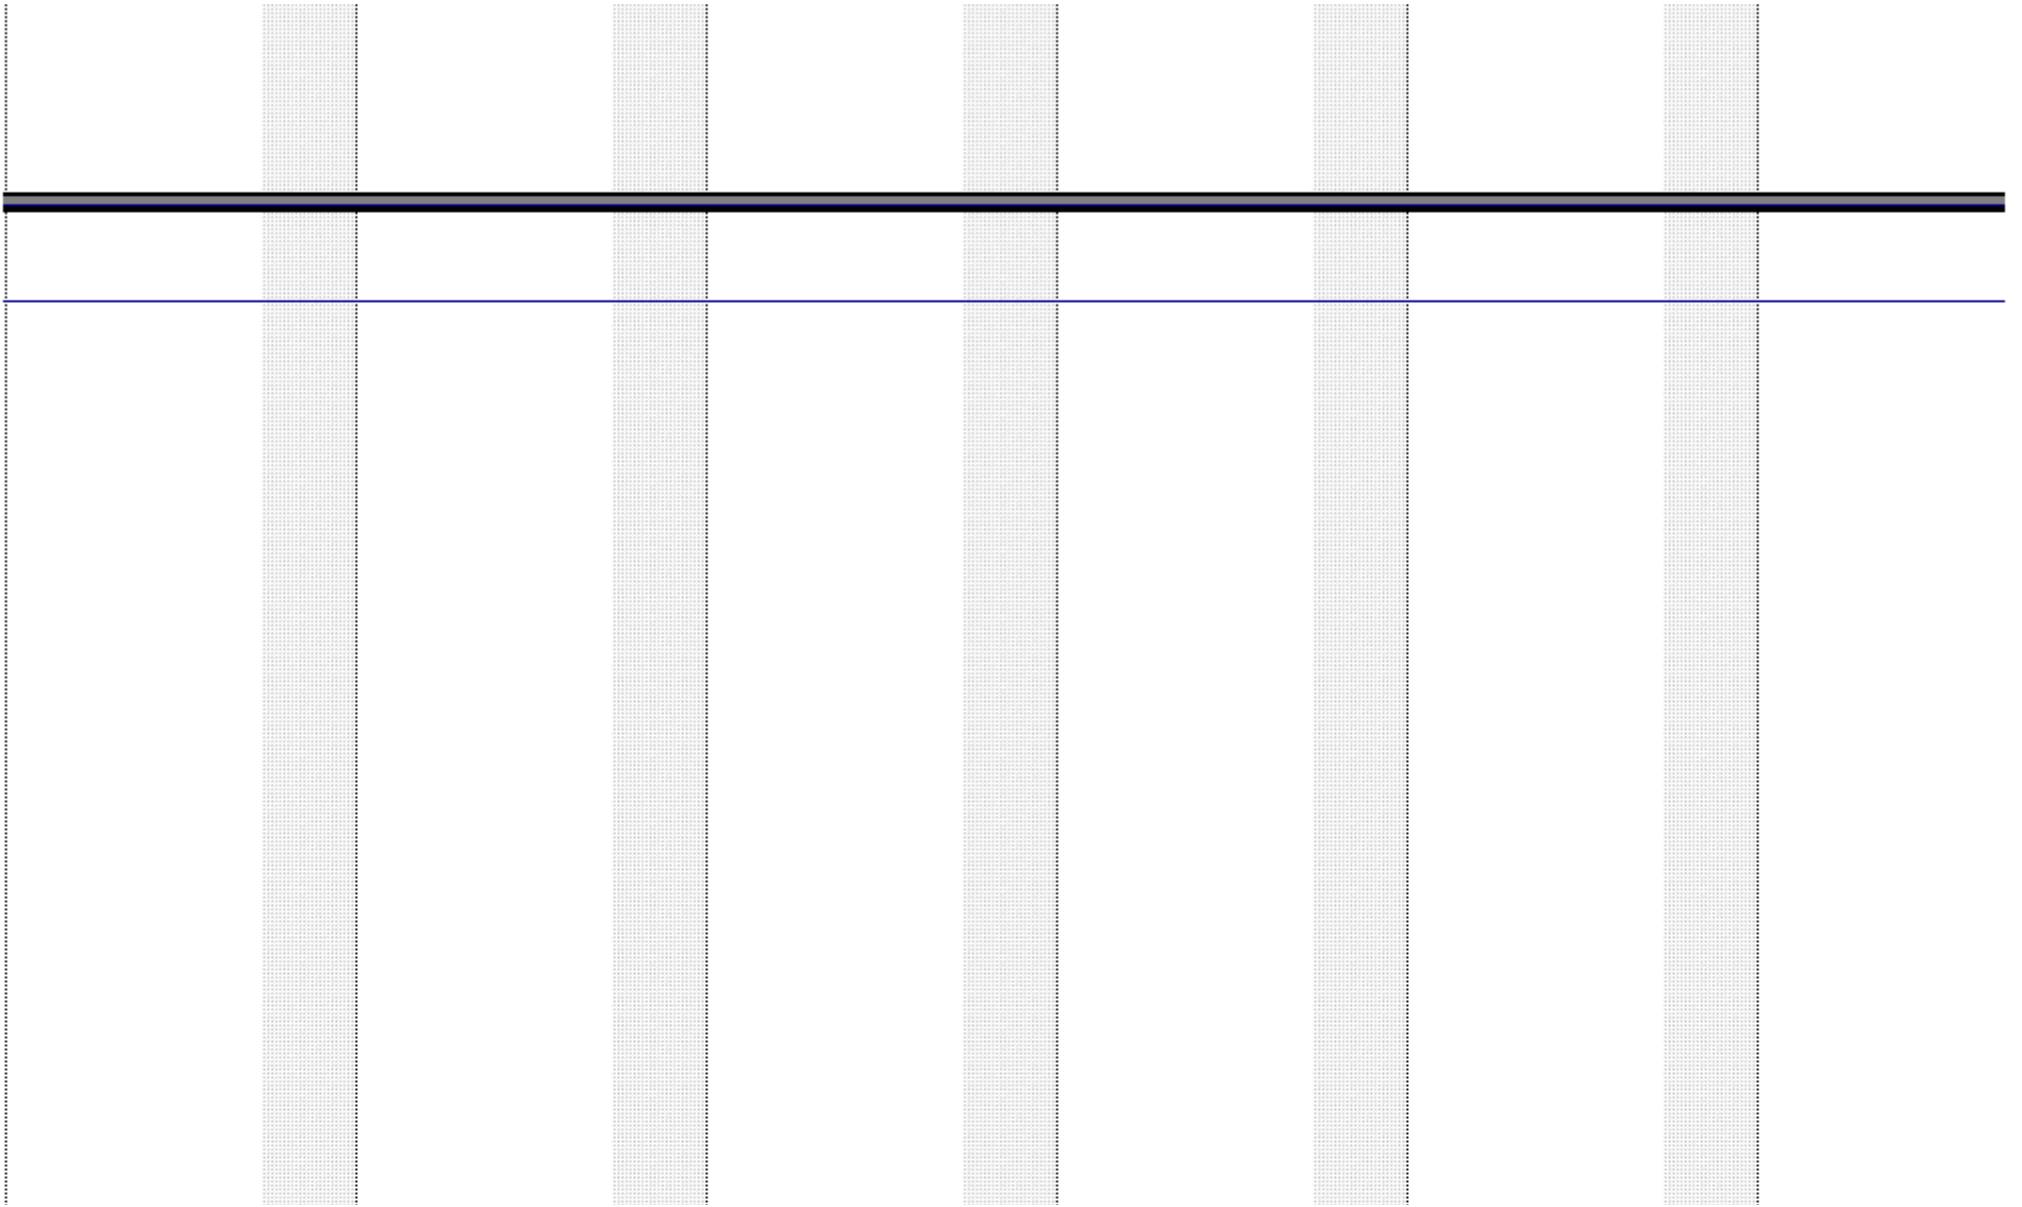

.....

.....


.....




.....

.....

.....

[illegible]

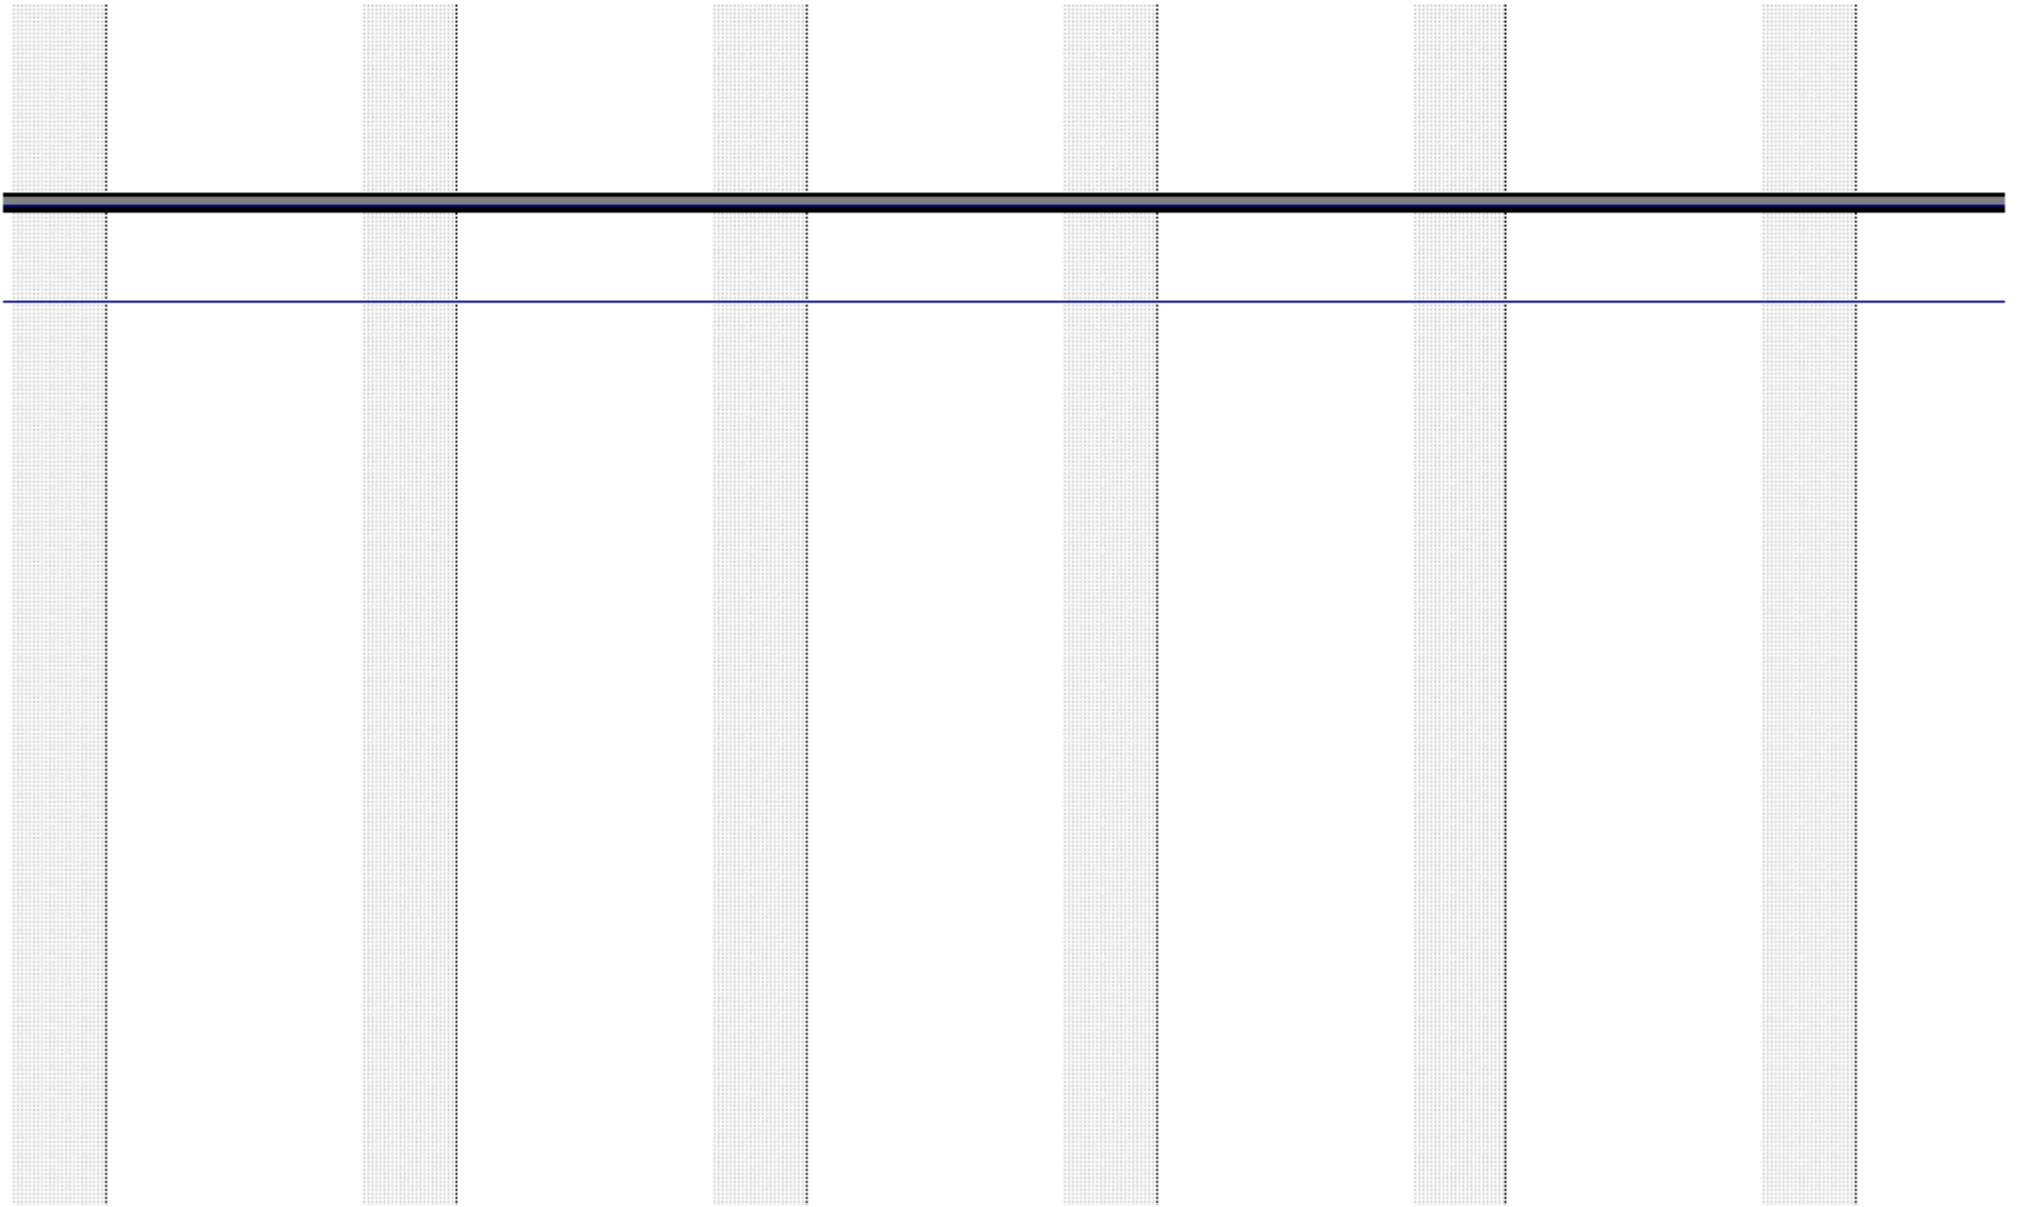



'18				Oct 8 - Oct 14 '18				Oct 15 - Oct 21 '18				Oct 22 - Oct 28 '18				Oct 29 - Nov 4 '18				Nov 5 - Nov 11 '18											
J	V	S	D	L	M	X	J	V	S	D	L	M	X	J	V	S	D	L	M	X	J	V	S	D	L	M	X	J	V	S	D
05/11/2018																															
05/11/2018																															
05/11/2018																															

